

Our New School Site – February update



The following work has been completed recently:

- Data cable install now ongoing through the building, server room and hub rooms being prepped
- Carpentry works ongoing
- Fire alarm cabling ongoing all floors
- Final plaster boarding to second floor, stair cores and sports hall
- Plastering to all levels including sports hall
- Ducting ongoing to all floors and lagged, roof operations commenced.
- First fix sliding door partitions installed
- Vinyl flooring to second floor science
- Fire stopping now ongoing
- Plumbing systems to toilets has commenced
- Concrete flooring to showers and floors complete
- Lift now installed to main building
- Ceiling grids have now commenced
- Sports field operations have now commenced after a recent dry period.
- Hygienic cladding underway
- Main kitchen extract canopy installed

Recent photographs



bam Date 1/3/21
Derby Cathedral School HMD.0313



Main dining atria now boarded ready for plaster



Cladding works ongoing to sports hall



Typical classroom ready for ceiling and flooring



Recent photographs



West, south and north
nearing scaffold strike
once parapet capping is
complete.



Ceiling tiles and grid stored in
sports hall, last delivery of
plasterboard in storage



Recent photographs



←
Pipework in
Foodtech now
being installed

Science
Terrace
brickwork
completed,
scaffold struck,
prep for roof
covering →



Main hall
decorations
and first fix
sliding
partition
install
←

Recent photographs



↑ Electrical and Mechanical ceiling works ongoing. Note casing protection in place



↑ Permeant edge protection being installed



Server rooms painted with casings, data being installed

Main kitchen canopy install and hygienic cladding installed



Recent photographs



IPS track and panels have now commenced to the toilets with bulkhead ceilings complete



DPM to floors ready for vinyl



Lagging to ductwork well underway with many areas completed



IPS for toilet sinks



Recent photographs



bam Date 1/3/21
Derby Cathedral School HMD.0313



Corridors highlighting carpentry, data install



Heated rooms have allowed floor prep, dpm and latex screed to science



Recent photographs



Date 1/3/21
Derby Cathedral School HMD.0313



Vinyl now being laid to science classrooms →



↑ Sample room, note carpet tiles ready for laying



More vinyl in Science ↑

Recent photographs



Typical class rooms all floors, timber, paint and first fixed




Corridors ready for plaster



Main feature window



Data cable laying on second floor

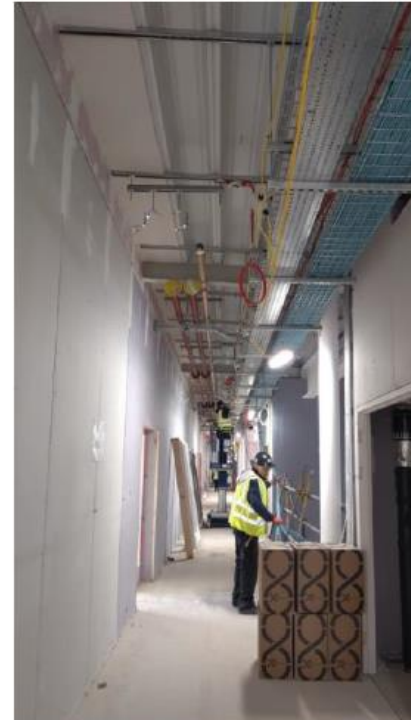

Roof duct supports ready for crane lift 2/3/21

Recent photographs



Shower
drainage
installed and
screed



Cladding sheets and roof
capping ongoing to the sports
hall. Man safe system now
installed



Main kitchen extract being installed



Recent photographs



bam Date 1/3/21
Derby Cathedral School HMD.0313



IPS to
toilets
➔



Sports hall
decorations
ongoing
➔



Fire alarm
installation
➔



Sports hall
changing
decorations
ongoing
↑

What is happening next...

- Fixed Furniture install
- Main entrance final curtain walling
- Carpet to classrooms
- External hardscapes
- Completion of Server and Hub rooms
- Strike scaffold to main building
- M&E works to sports hall.

Recent photographs

Congratulations to the building team for being awarded the regional health & safety award by their company, BAM

